

RUNNYMEDE ROUNDABOUT IMPROVEMENT PROJECT

Welcome to issue 6 of the Runnymede Roundabout project e-newsletter which will give you information and the latest updates on this major project.

21 December 2017

Upcoming works

A series of night works will take place from Monday 8th January 2018 on The Avenue and around the roundabout.

- The foundation level of resurfacing material will be trafficked to allow for traffic management to be changed in January 2018.
- Pavement works will continue along A308 Windsor Road.
- The diversion of an Affinity Water main pipe is due to be complete in January 2018.
- Vodafone have planned night works on the Monday 8th, Tuesday 9th and Wednesday 10th January 2018 to finish works in the Avenue.
- Concrete works are due to be completed on the A30 on the central reservation in readiness for Vehicle Restraint System installation.
- The installation of a Vehicle Restraint System on the A30.
- The asphalt foundation to be laid on the new third lane on the A30.

Ongoing construction works


- Works to the slip road to the M25 junction 13 roundabout continue with the intention of commencing works on lane 2 in January 2018.
- The U-turn facility will remain closed as the asphalt to binder levels are being laid.
- Drainage around the main part of the roundabout is almost complete.
- Installation of new kerbing to the main part of the roundabout is now substantially complete.

Holiday closure dates

The scheme of works will be closed over Christmas from Friday 22nd December 2017 until Monday 8th January 2018. During this period the site will be monitored to ensure it remains safe. Have a Merry Christmas and a Happy New Year!



The pictures above show the new U turn facility and the new service vehicle bay on the north side of the roundabout.

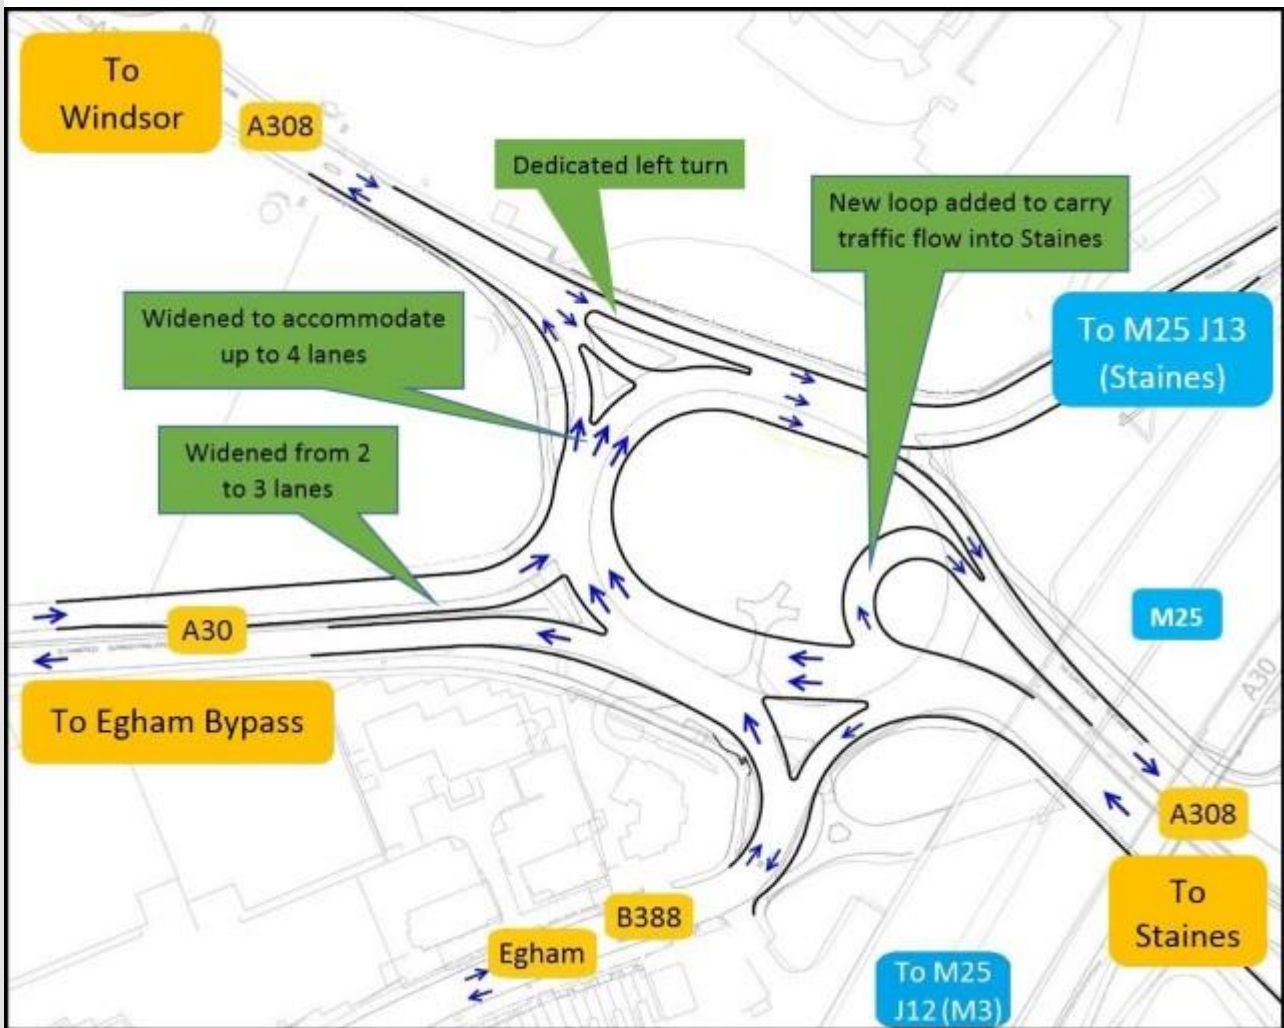

Based upon the Ordnance Survey mapping with the permission of the Controller of Her Majesty's Stationery Office ©Crown copyright. Unauthorised reproduction infringes Crown copyright and may lead to prosecution or civil proceedings. Surrey County Council LA0758722002

What's changing on the roundabout and why

We will be:

- Widening and resurfacing the lanes around the roundabout. Providing a new 'U-turn' facility between the A30 'Glanty Loop' off-slip and the A308 to Staines.
- Introducing signals at each of the junctions.

- Installing toucan crossing facilities across the junction arms.
- Creating a new shared-use path to the north-east of the roundabout.

By widening the lanes, resurfacing them and putting in traffic lights we're aiming to reduce congestion and help improve journey times. The new loop to Staines means that 800 fewer vehicles will join the roundabout in rush hours which will cut queues. Better facilities for pedestrians and cyclists will also make their journeys easier and safer.

Stay up to date

Please check your route before setting off on your journey. You can do this by visiting www.A30.today, by checking www.roadworks.org or by following [@SurreyTravel](https://twitter.com/SurreyTravel) on Twitter.

Useful Links: [Contact us](#) | [Tell a colleague](#) | [Unsubscribe](#)

Published by Works Communication Team, Highways, Surrey County Council. ©2017 Surrey County Council.
